

# School Board Workshop 12/17/19: Transitional Campus



## Revitalizing Our Schools



- Half Cent for Schools initiative approved by voters in 2018
- Between Half-Cent and 1½
  mill capital outlay funding,
  nearly \$500 million will be
  invested in school facilities
  over the next 12-15 years
- Focus is on revitalizing existing schools

## Revitalizing Our Schools


- Projects prioritized based on a wide variety of factors including age of facility, condition of facility, use of space, etc.
- Projects currently underway at 19 schools (planning and construction)



### Revitalizing Our Schools

- First four large-scale projects: Metcalfe Elementary School, Idylwild Elementary School, Bishop Middle School, Elementary School I
- District's applications to demolish buildings at Metcalfe, Idylwild and Bishop approved by DOE
- Architects and construction managers have been hired for all four schools; designs under development
- Transition plans developed for Metcalfe (on-site) and Idylwild (Prairie View swing school site)

## **Prairie View Swing School**

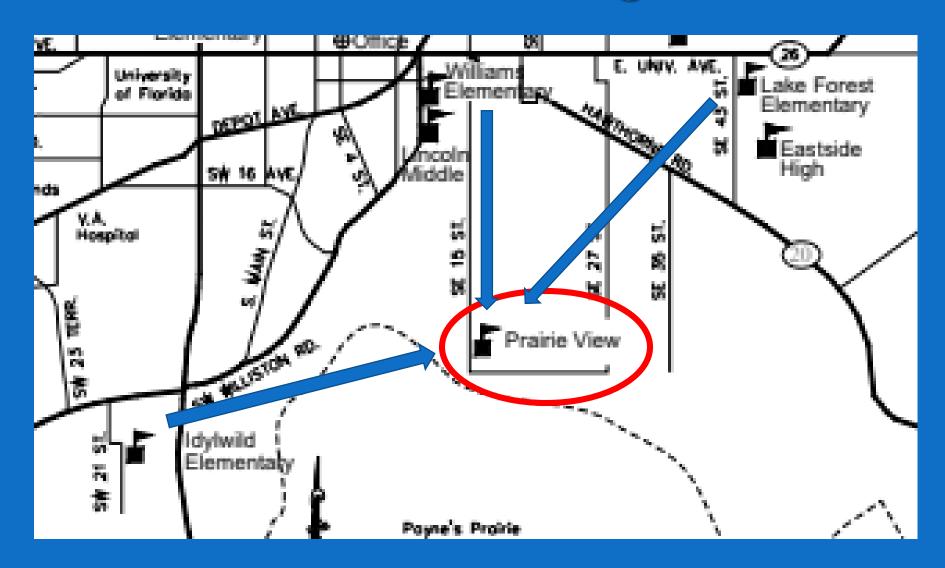

## Swing school vs. 'phasing'

- Keeps students/staff out of construction zone
- Limits risk of utilities interruptions and other disruptions to instruction
- Work can continue during testing periods
- Projects completed much sooner
- Much more cost effective, meaning more
   \$ can be spent on permanent projects

## Modular School









## Facts and figures

- Modular school costs \$1 million/year to lease, depending on number/type of buildings
- Cost of setting up a modular school is about \$3 million, depending on number/type of buildings and location
- Site work/installation takes about six months

Due to time and costs of building and relocating modular schools, they need to be used more than once at the same location

### Other considerations

- Larger spaces needed?

   (dining area, band room, media center, etc.)
- Student population
- Grade levels
- Special programs
- Parking and traffic



Transportation is provided

## Howard Bishop Redevelopment

## Projected cost: \$18.1 million



- Demolish 18 buildings: classroom buildings, tech labs, computer skills labs, dining/kitchen, restroom buildings
- Construct 32 new classrooms
- Construct 2 new science classrooms/labs

- Construct 2 new technology/business labs
- Construct new kitchen/ dining/multi-purpose building
- Renovate/modernize 7 existing classrooms

## Progress to date

- Architect Paul Stresing, Inc. hired to design redeveloped school; design under development
- Public input session held August 22
- Faculty input session held October 11
- Community School input session held October 28
- D.E. Scorpio Construction hired as project construction manager
- Application to demolish buildings approved by the Florida Department of Education in mid-November







### **Initial Considerations**

- Review of best practices in other school districts, including site visits
- Splitting students
- Wild Spaces/Public Places project at Bishop
- Impact of phasing Bishop project
- Use of Lincoln Middle School
- Use of transition school for three projects

## Bishop Transition Options: Swing School at Westwood Middle



## Swing School at Westwood Middle

#### **Considerations:**

- Most Bishop students would take buses to Westwood campus (estimated 18-20 buses)
- Staggered start/dismissal times and other strategies to address traffic congestion, including law enforcement support and additional school staff
- Students/staff off Bishop campus during construction
- Westwood students move into modular school after Bishop project completed, Littlewood students move in after Westwood is completed

## Swing School at Westwood Middle

 Discussions between district staff, design professionals and City of Gainesville staff, including representatives from:

Wild Spaces/Public Places

Parks and Recreation

Gainesville Fire Rescue


Gainesville Regional Utilities

 Topics included: Use of Westside Park for bus drop off, overflow parking, recreational spaces; utilities access; safety and security, emergency services;

## Swing School at Westwood Middle

- Meeting with City Manager and staff members on November 26
- Included information about a renovation/drainage project at Westside Park, delay of Wild Spaces/Public Places project at Howard Bishop Middle, offer of Citizens' Park as a potential swing school site, offer to lease RTS bus compound
- PTO meeting December 3 at Westwood Middle included concerns about traffic/parking and other issues (PTSA meeting at Bishop on December 11)

## Bishop Transition Options: Swing School at Bishop Middle

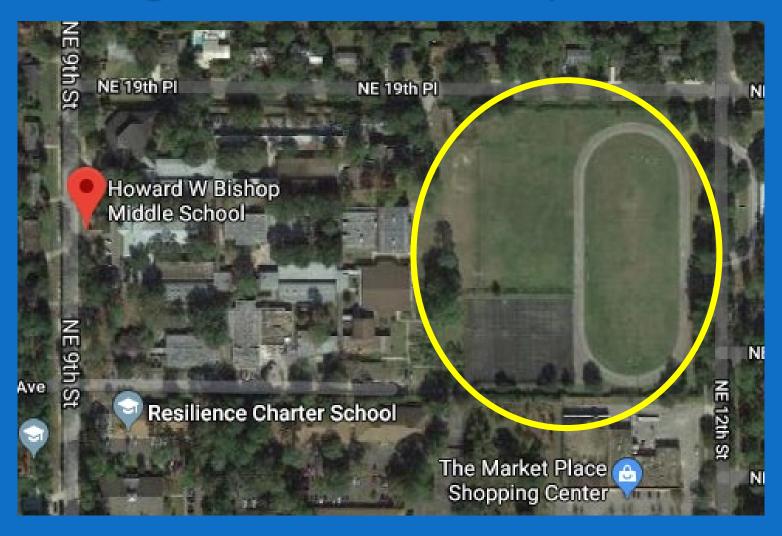


## Bishop Transition Options: Swing School at Bishop Middle

#### **Considerations:**

- After Bishop students move into their new facilities, students from other schools would be transported to modular campus while their schools are renovated
- Size/infrastructure for Bishop <u>and</u> other school populations
- Staggered start/dismissal times and other strategies to address traffic congestion
- Impact on Wild Space/Public Places improvement timeline

## Bishop Transition Options: Swing School at Citizens' Park

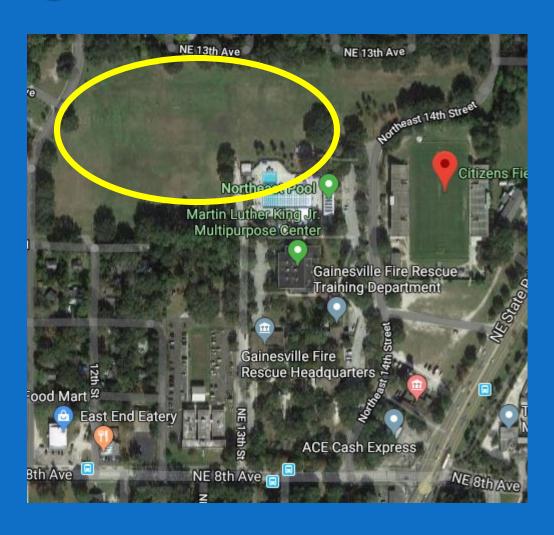

## Swing School at Citizens' Park

#### **Considerations:**

- Feasibility of site (size, utilities, etc.)
- Availability of site long-term
- Significantly higher costs
- Increased transportation requirements
- Traffic, parking, safety

## Other suggested sites

A. Quinn Jones: too small

**District Office:** 120-year-old building, expensive and time-consuming to renovate into a school, code issues, etc.; grounds too small

ACPS Transportation Compound: Active industrial area, would require environmental study and demolition of compound (cost, Castaldi, etc.); additional cost to lease RTS bus facility

**Fairgrounds:** Too close to Gainesville Regional Airport (F.S. 1013.36 says no school in flight path)

Job Corps Building: Too close to airport, active industrial area


## Next Steps

- Ongoing communication with City of Gainesville regarding site options
- Feasibility studies, including traffic reviews, on potential sites

The goal is to avoid or minimize any potential delay in beginning construction while providing the best possible situation for students.

## Facilities Story Map

List of school projects, timelines and progress available on the district's website (sbac.edu)

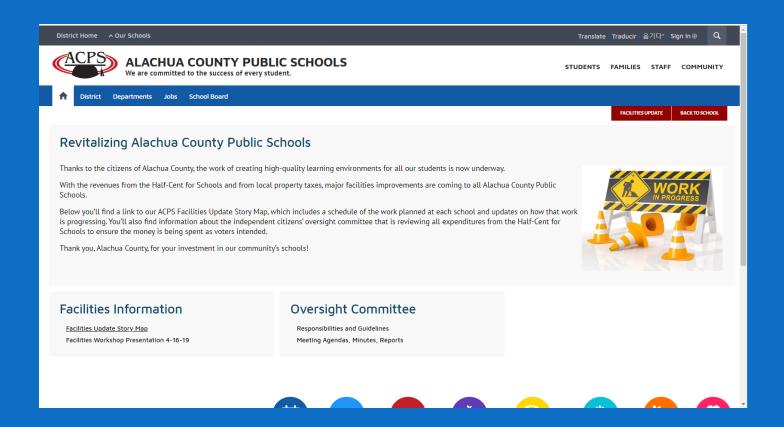

## Questions?
